


Soku Gasplant AG2 Controls upgrade Schedule

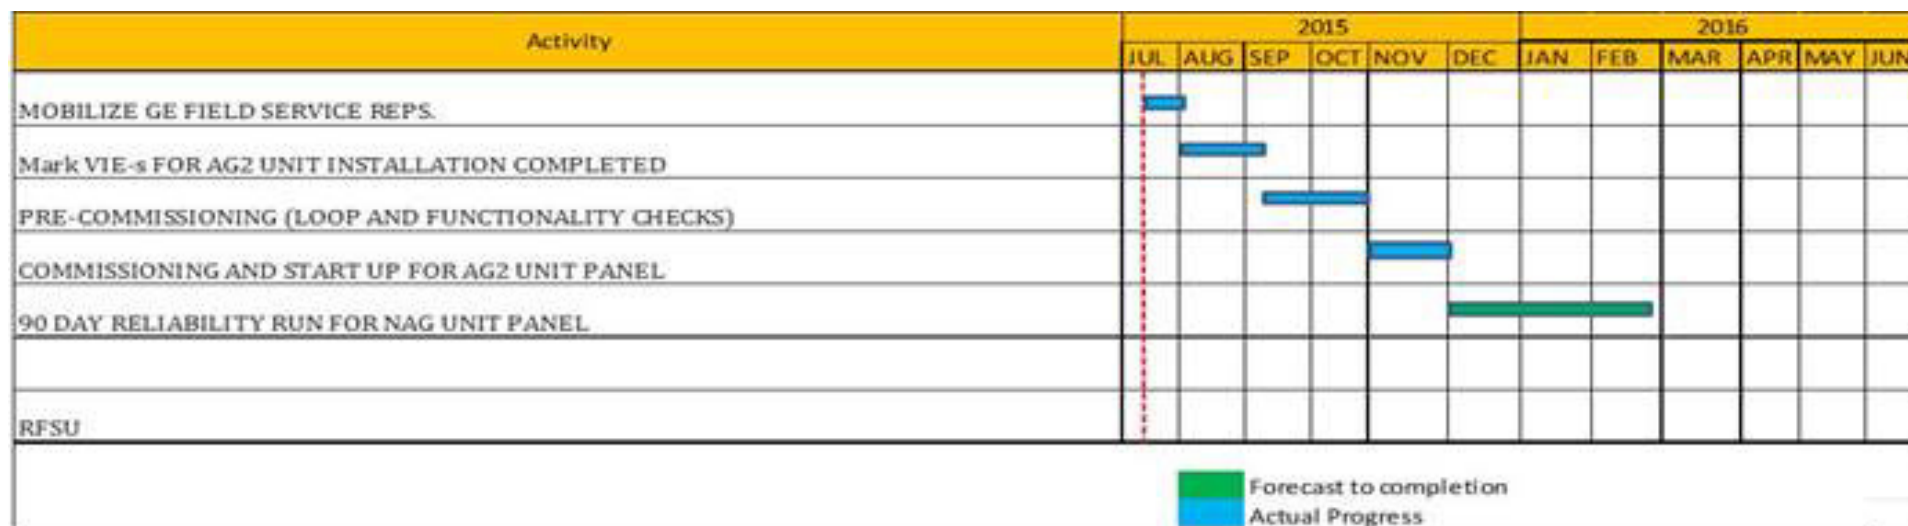

NOTE:

This schedule is based on the following assumptions:

1. If you give us the AG2 by mid July 2015 (July 15 is mid-July)
2. GE FSRs need 2 weeks minimum to mobilize to site
3. Estimated duration for AG2 installation and pre-comm. is approx. 90days, assuming very little complications; and this does not include commissioning (approx. 30 days), start-up & reliability run test (90 days), which altogether is about 210 days.
4. Also note that reliability run test may now run into 2016, prompting contract extension for GE contract which ends in 2015.
5. Also note that Alcon may need some time to engage new technicians as the current personnel will be fully engaged within this period completing the Instrument scope for NAG Compression which is ramping up to peak level and final commissioning the NAG systems

Schedule above was extracted from the AG2 Controls upgrade position paper already endorsed by key stakeholders including the GMP
