


ALAKIRI 36 & 37 PROJECT PLAN		
	Duration (Days)	
		26
Wells Activities		
Offline RU on Barge in Jetty(Mobilization)	7	
Alakiri 36 well lift		
Move and position barge	2	
RU CT & N2 spread + lift well to live	3	
Alakiri 37 well lift		
Move from ALAK 36 to ALAK 37 and position barge	1	
RU CT & N2 spread + lift well to live	3	
Demobilize CT spread	1	
Alakiri 36 clean up and MRT		
Mobilize Welltest Barge to paltform	1	
Carry out well clean up	1	
RU SL and carry SG survey + Install guages in RN Nipple	1	
Carry out MRT	1	
Final build up	1	
Pull guages and carry out SG	1	
Secure well and handover same	1	
Alakiri 37 clean up and MRT		
Move and position barge	1	
Carry out well clean up	1	
RU SL and carry SG survey + Install guages in RN Nipple	1	
Carry out MRT	1	
Final build up	1	
Pull guages and carry out SG	1	
Secure well and handover same	1	
Demobilize well test spread	1	
Total	32	

LEGE



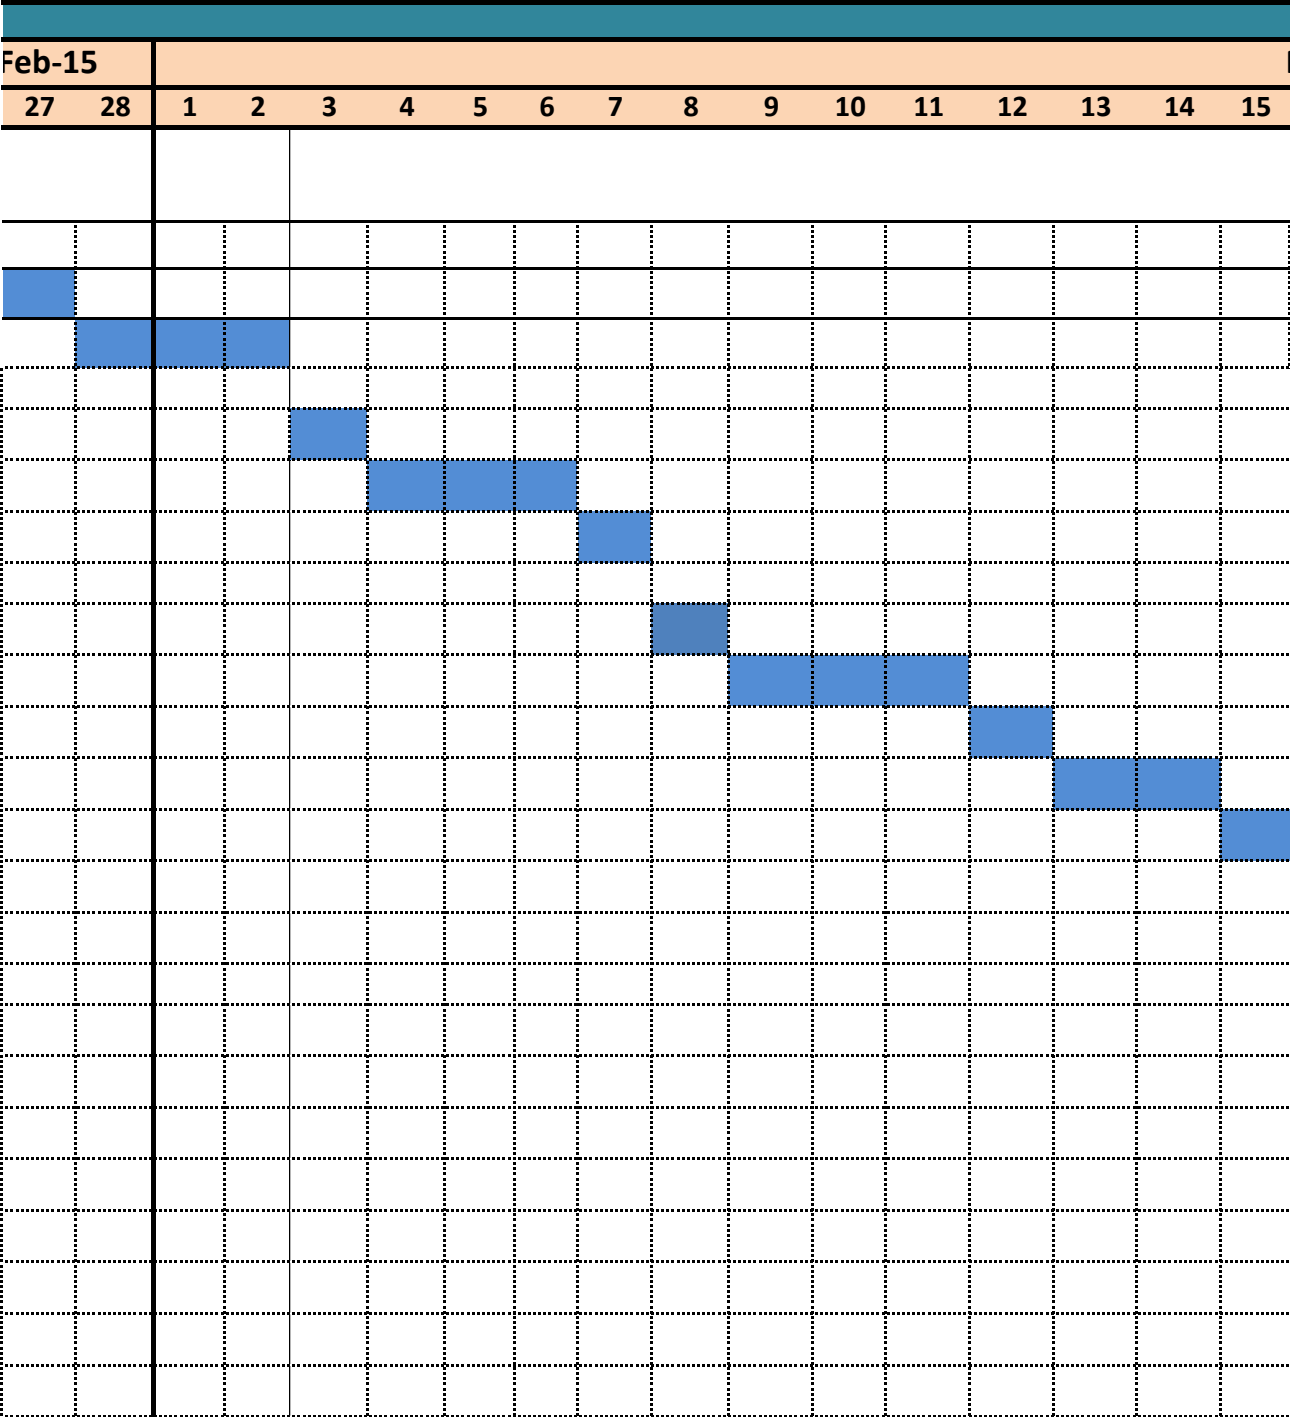

Activity duration to the ALAK flare

16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
----	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----

[illegible]
