


ALAKIRI 36 & 37 PROJECT PLAN

	Duration (Days)	
		7
Wells Activities		
Offline RU on Barge in Jetty (mobilization)	7	
Alakiri 36 well int		
Move and position barge	2	
RU CT & N2 spread + lift well to live	3	
Alakiri 37 well int		
Move from ALAK 36 to ALAK 37 and position barge	1	
RU CT & N2 spread + lift well to live	3	
Demobilize CT spread	1	
Alakiri 36 clean up and MRT		
Mobilize Welltest Barge to platform	1	
Carry out well clean up	1	
RU SL and carry SG survey + Install gauges in RN Nipple	1	
Carry out MRT	1	
Final build up	1	
Pull gauges and carry out SG	1	
Secure well and handover same	1	
Alakiri 37 clean up and MRT		
Move and position barge	1	
Carry out well clean up	1	
RU SL and carry SG survey + Install gauges in RN Nipple	1	
Carry out MRT	1	
Final build up	1	
Pull gauges and carry out SG	1	
Secure well and handover same	1	
Demobilize well test spread	1	
Total	32	

LEGE



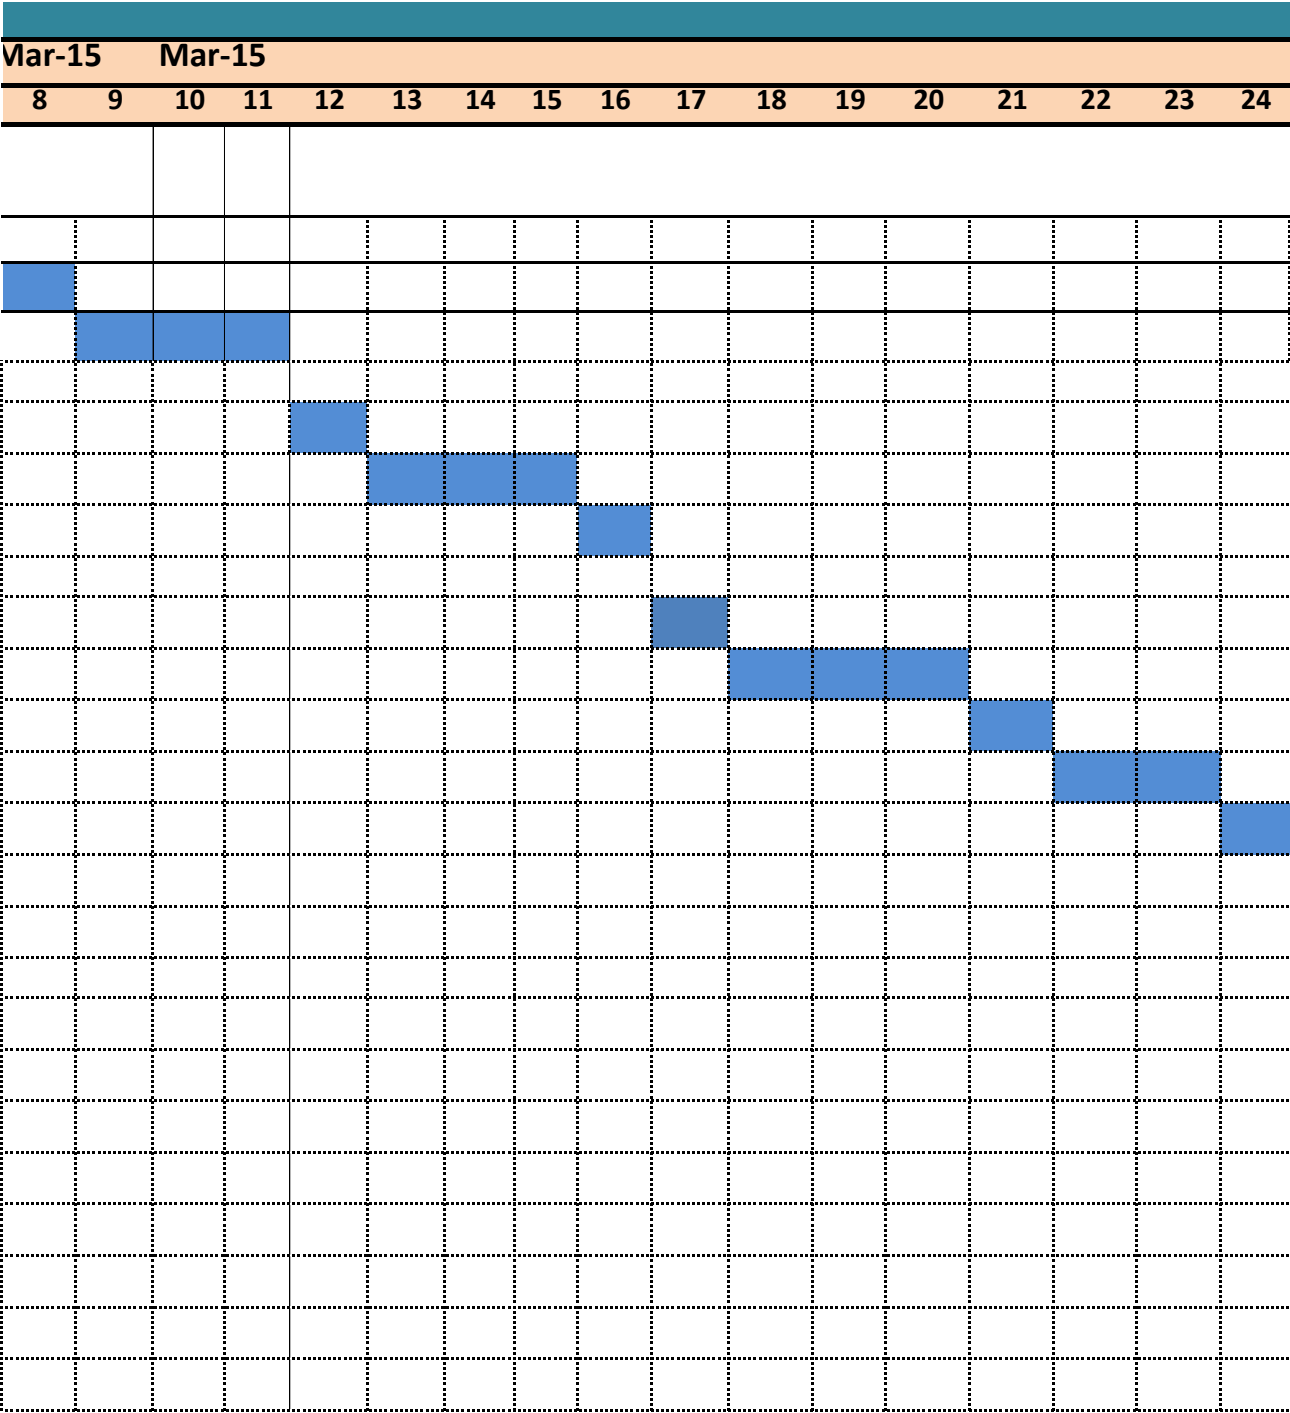

ND

Activity duration to the ALAK flare

[illegible]
